



A map of the region around Colima, Mexico. The city of Colima is labeled in the top left corner. A yellow circle with a black bridge icon and the text "Puente 'La Presa Trancas'" is located in the center of the map. The map shows various towns and cities, including La Salada, Caután, Ixtlahuacán, Zinacmitlán, San Marcos, San Gabriel, Agua de la Virgen, Las Tunas, Las Conchas, Tecolapa, Caleras, Tecomán, and Estapilla. Major roads are marked with numbers 110, 19, 243, 185, and 78. A red arrow points north in the bottom right corner.

Tramo	Empresas
Construcción del Puente La Presa Trancas	• Contratista: GRUPO FIRME DE MÉXICO, S.A DE C.V, CONSTRUCTORA SANTOS CHISUM, S.A DE C.V Y CONSTRUCCIONES Y TERRACERÍAS VANGUARDIA, S.A DE C.V • Supervisión: ANMA INGENIERÍA, SA DE CV


Puente La Presa Trancas

Colima

ACTUALIZADA 30/04/26

Avance: Programado, Físico y Financiero (%)

Elemento	Intervención	Ejecutado acumulado	Faltante	24/04/26 al 30/04/26	
				Programado	Ejecutado
Preliminares					
Desmonte y Despalme (Ha)	0.83	0.83	0.00	0.00	0.00
Subestructura					
Pilas de cimentación (Perforación). Pza.	26.00	26.00	0.00	0.00	0.00
Pilas de cimentación (Armado). Pza.	26.00	26.00	0.00	0.00	0.00
Pilas de cimentación (Colado). Pza.	26.00	26.00	0.00	0.00	0.00
Columnas. Pza.	2.00	2.00	0.00	0.00	0.00
Construcción de cabezales y bancos. Pza.	4.00	4.00	0.00	0.00	0.00
Superestructura					
Trabes pretensadas AASHTO TIPO VI (Pza) (Fabricación)	18.00	18.00	0.00	0.00	0.00
Trabes pretensadas AASHTO TIPO VI (Pza) (Montaje)	18.00	18.00	0.00	0.00	0.00
Colado de diafragma y losa. M3	197.10	197.00	0.00	0.00	0.00
Carpeta asfáltica. M3.	220.00	220.00	0.00	0.00	0.00
Guarniciones, Banquetas y Parapetos. M3.	43.80	43.80	0.00	0.00	0.00
Accesos, señalamiento y Obras complementarias. M.	182.00	52.00	130.00	130.00	10.00

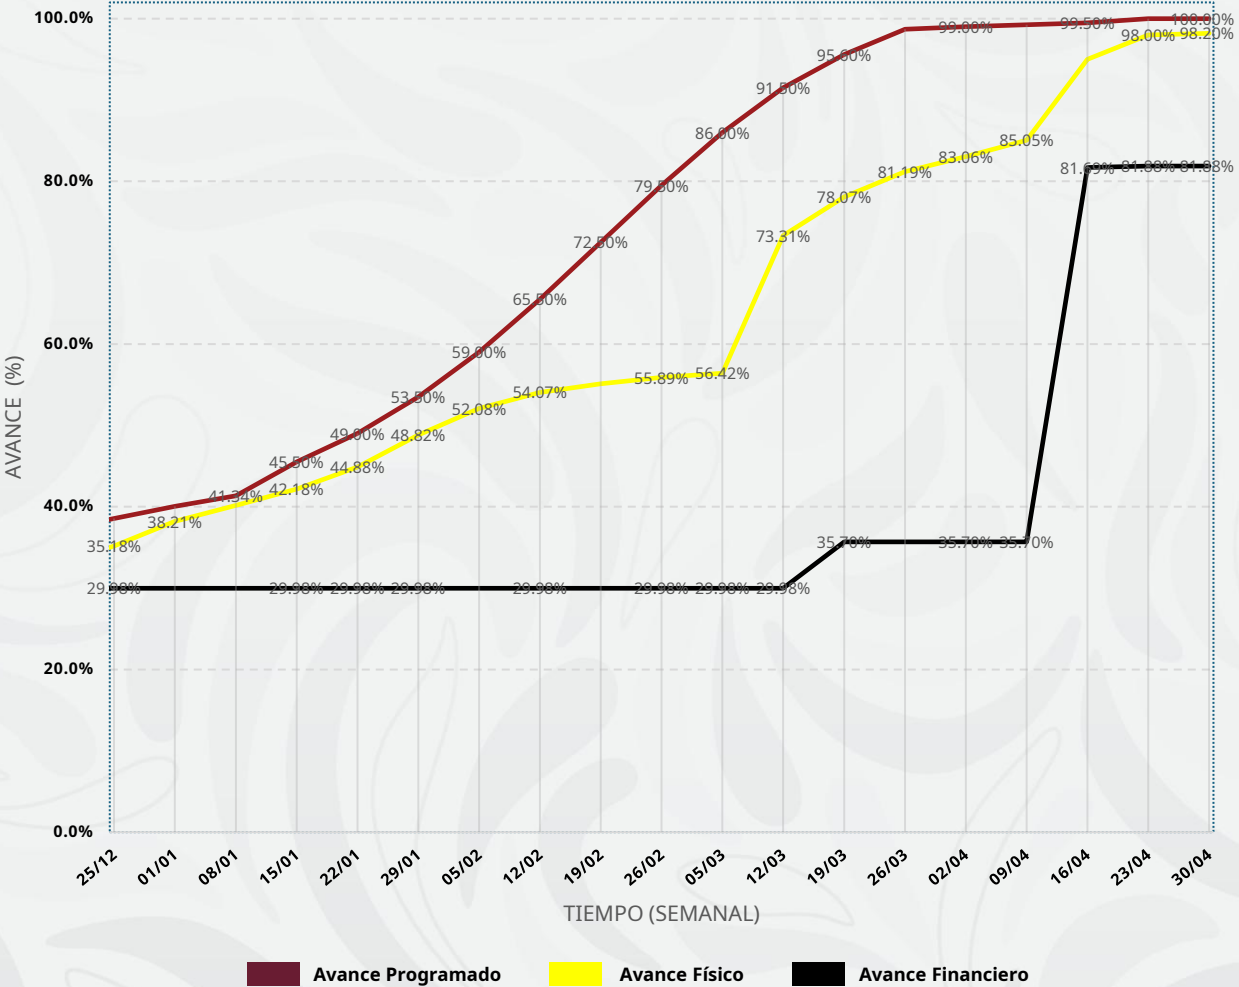

	17 al 23 de abril	24 al 30 de abril
Fuerza de Trabajo (personas)	29	29
Maquinaria	2	2
Frentes de trabajo	8	6
